



BIG Project Update

Progress to Date

And what's next

THE CITY OF


PRINCE RUPERT

Overview

- ~**2.5 km** of the identified priority 26 kms (almost 10%) have been **completed** to date (paving end of summer)
- **\$45 M committed or spent** of total **\$193 M Budget**
- **77 homes** with impacted/improved infrastructure replaced on Crestview/Bacon to date
- **\$9.6 M** in Quadrant 1 **design/early works**



This is over **3 times** what was replaced in 2023, and almost **8 times** what was replaced in 2022





BIG Project 2025 Focus Areas Design RFP - Priority 1

Date: 2025 / 8 / 8

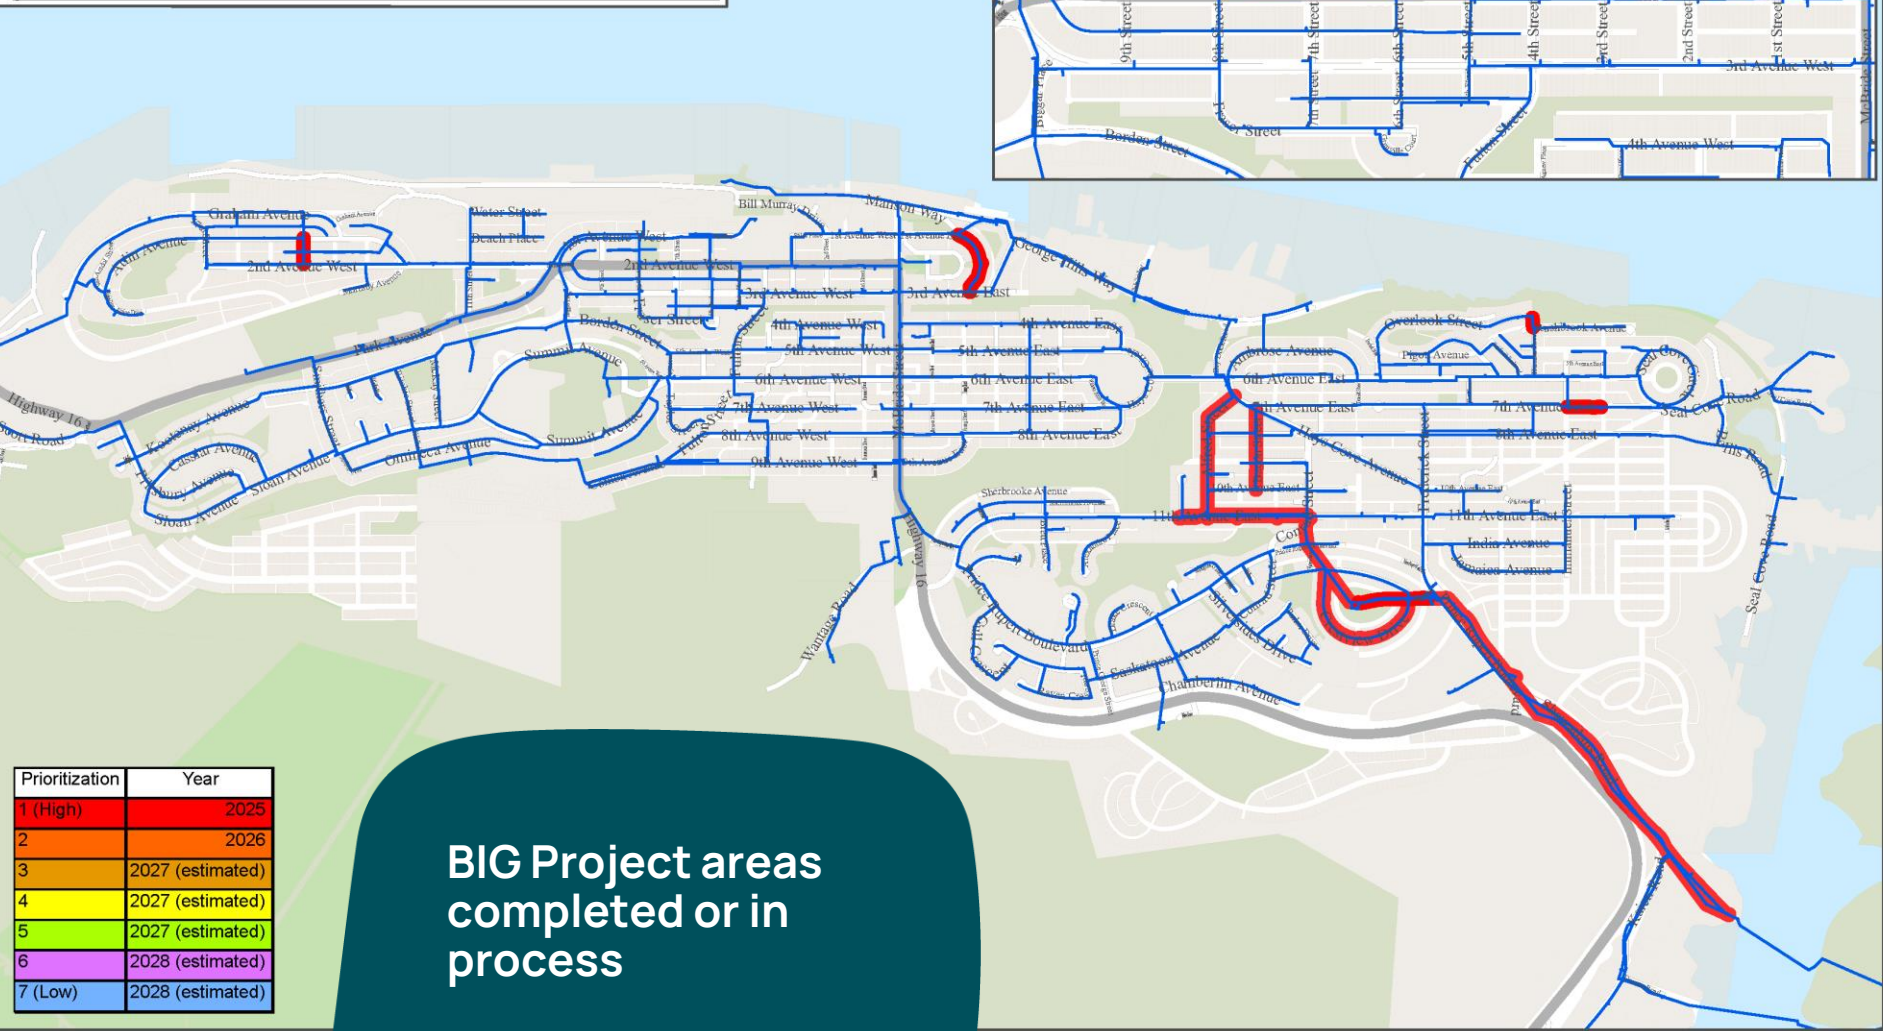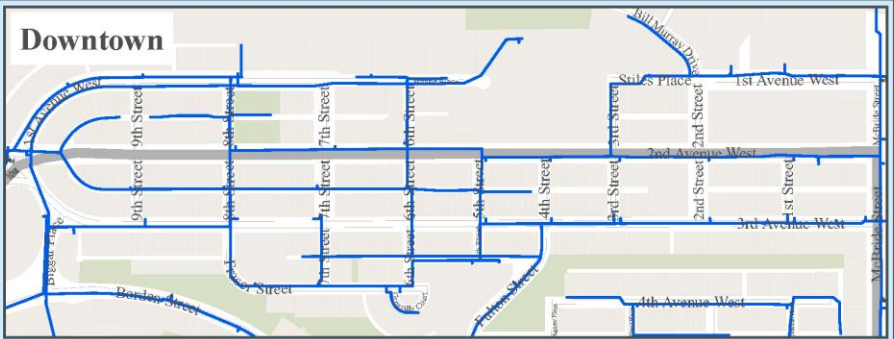

Prioritization	Year
1 (High)	2025
2	2026
3	2027 (estimated)
4	2027 (estimated)
5	2027 (estimated)
6	2028 (estimated)
7 (Low)	2028 (estimated)

BIG Project areas
completed or in
process

Applewhaite/Crestview


Status Update:

- 750 m length of pipe replaced (over 2024/2025)
- ~\$3.9 M final utility replacement cost (over 2024/2025 – not including paving)
- Curbing complete, paving scheduled for September

Bacon Street

Status Update:

- 265 m length of pipe
- \$2.53 M Budget
- Paving occurring in September

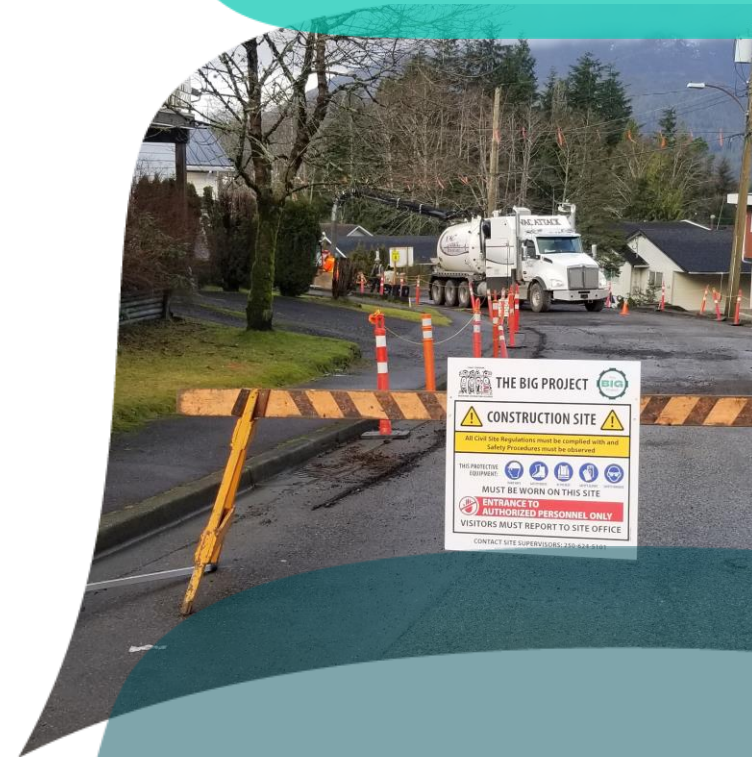

*Pause for
lessons*

Takeaways – Roundtable Session

**Following the first substantial
completion in residential area -
Crestview...**

Lessons learned

- Improve Communication between Contractor and City, along with residents when delays or issues arise
- Provide regular Community updates
- Additional feedback to be sought through survey



Shawatlans Road (Industrial Site Access)

Status Update:

- 1500 m (1.5 km)
- Complex area
 - Main water conveyance line into the community from the water supply
 - Multiple overlapping utilities underground at Frederick/Shawatlans
- Project has experienced delays due to supply chain issues and permitting.
- \$30 M anticipated cost



Upcoming Work:

Alfred Street

- 425 m length of pipe
- \$5.1 M Budget
- Project started with milling of pavement




11th Avenue


- 650 m length of pipe
- \$8.23 M Budget
- Designs complete and procurement issued



Where the \$\$ comes from

- \$77.2 M Federal Disaster Mitigation and Adaptation Fund
- \$65 M from the Province for Water Distribution Upgrades
- \$49.8 M from the City in approved borrowing + funding
- Additional value from the Province for replacement of utilities underneath the roundabout



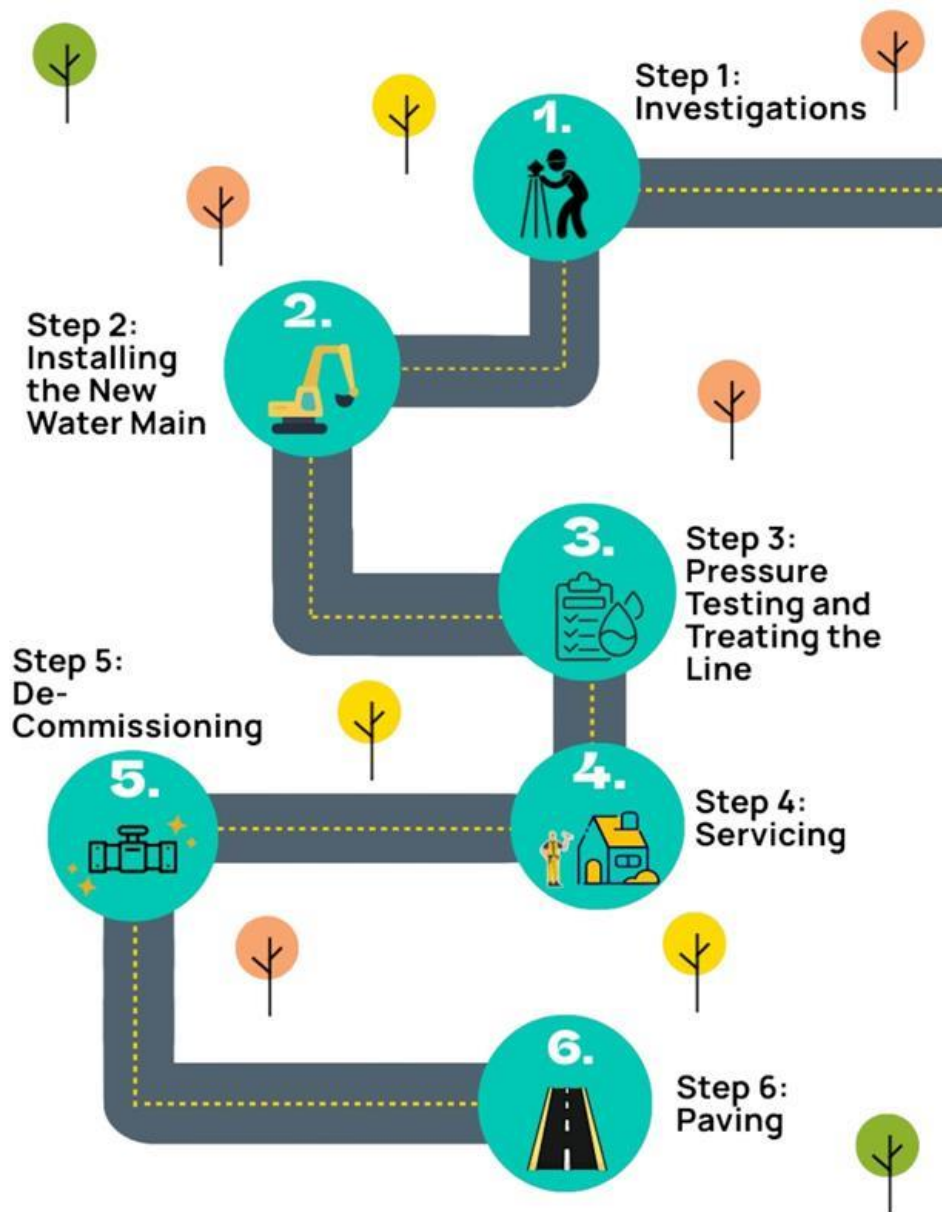

Communication Avenues:

For updates, resource links, FAQs and more:

engage.princerpert.ca/big

More in depth questions:

big@princerpert.ca

or

250-627-2850
